


Weekly Plan of Work
Week Commencing 31st August 2020

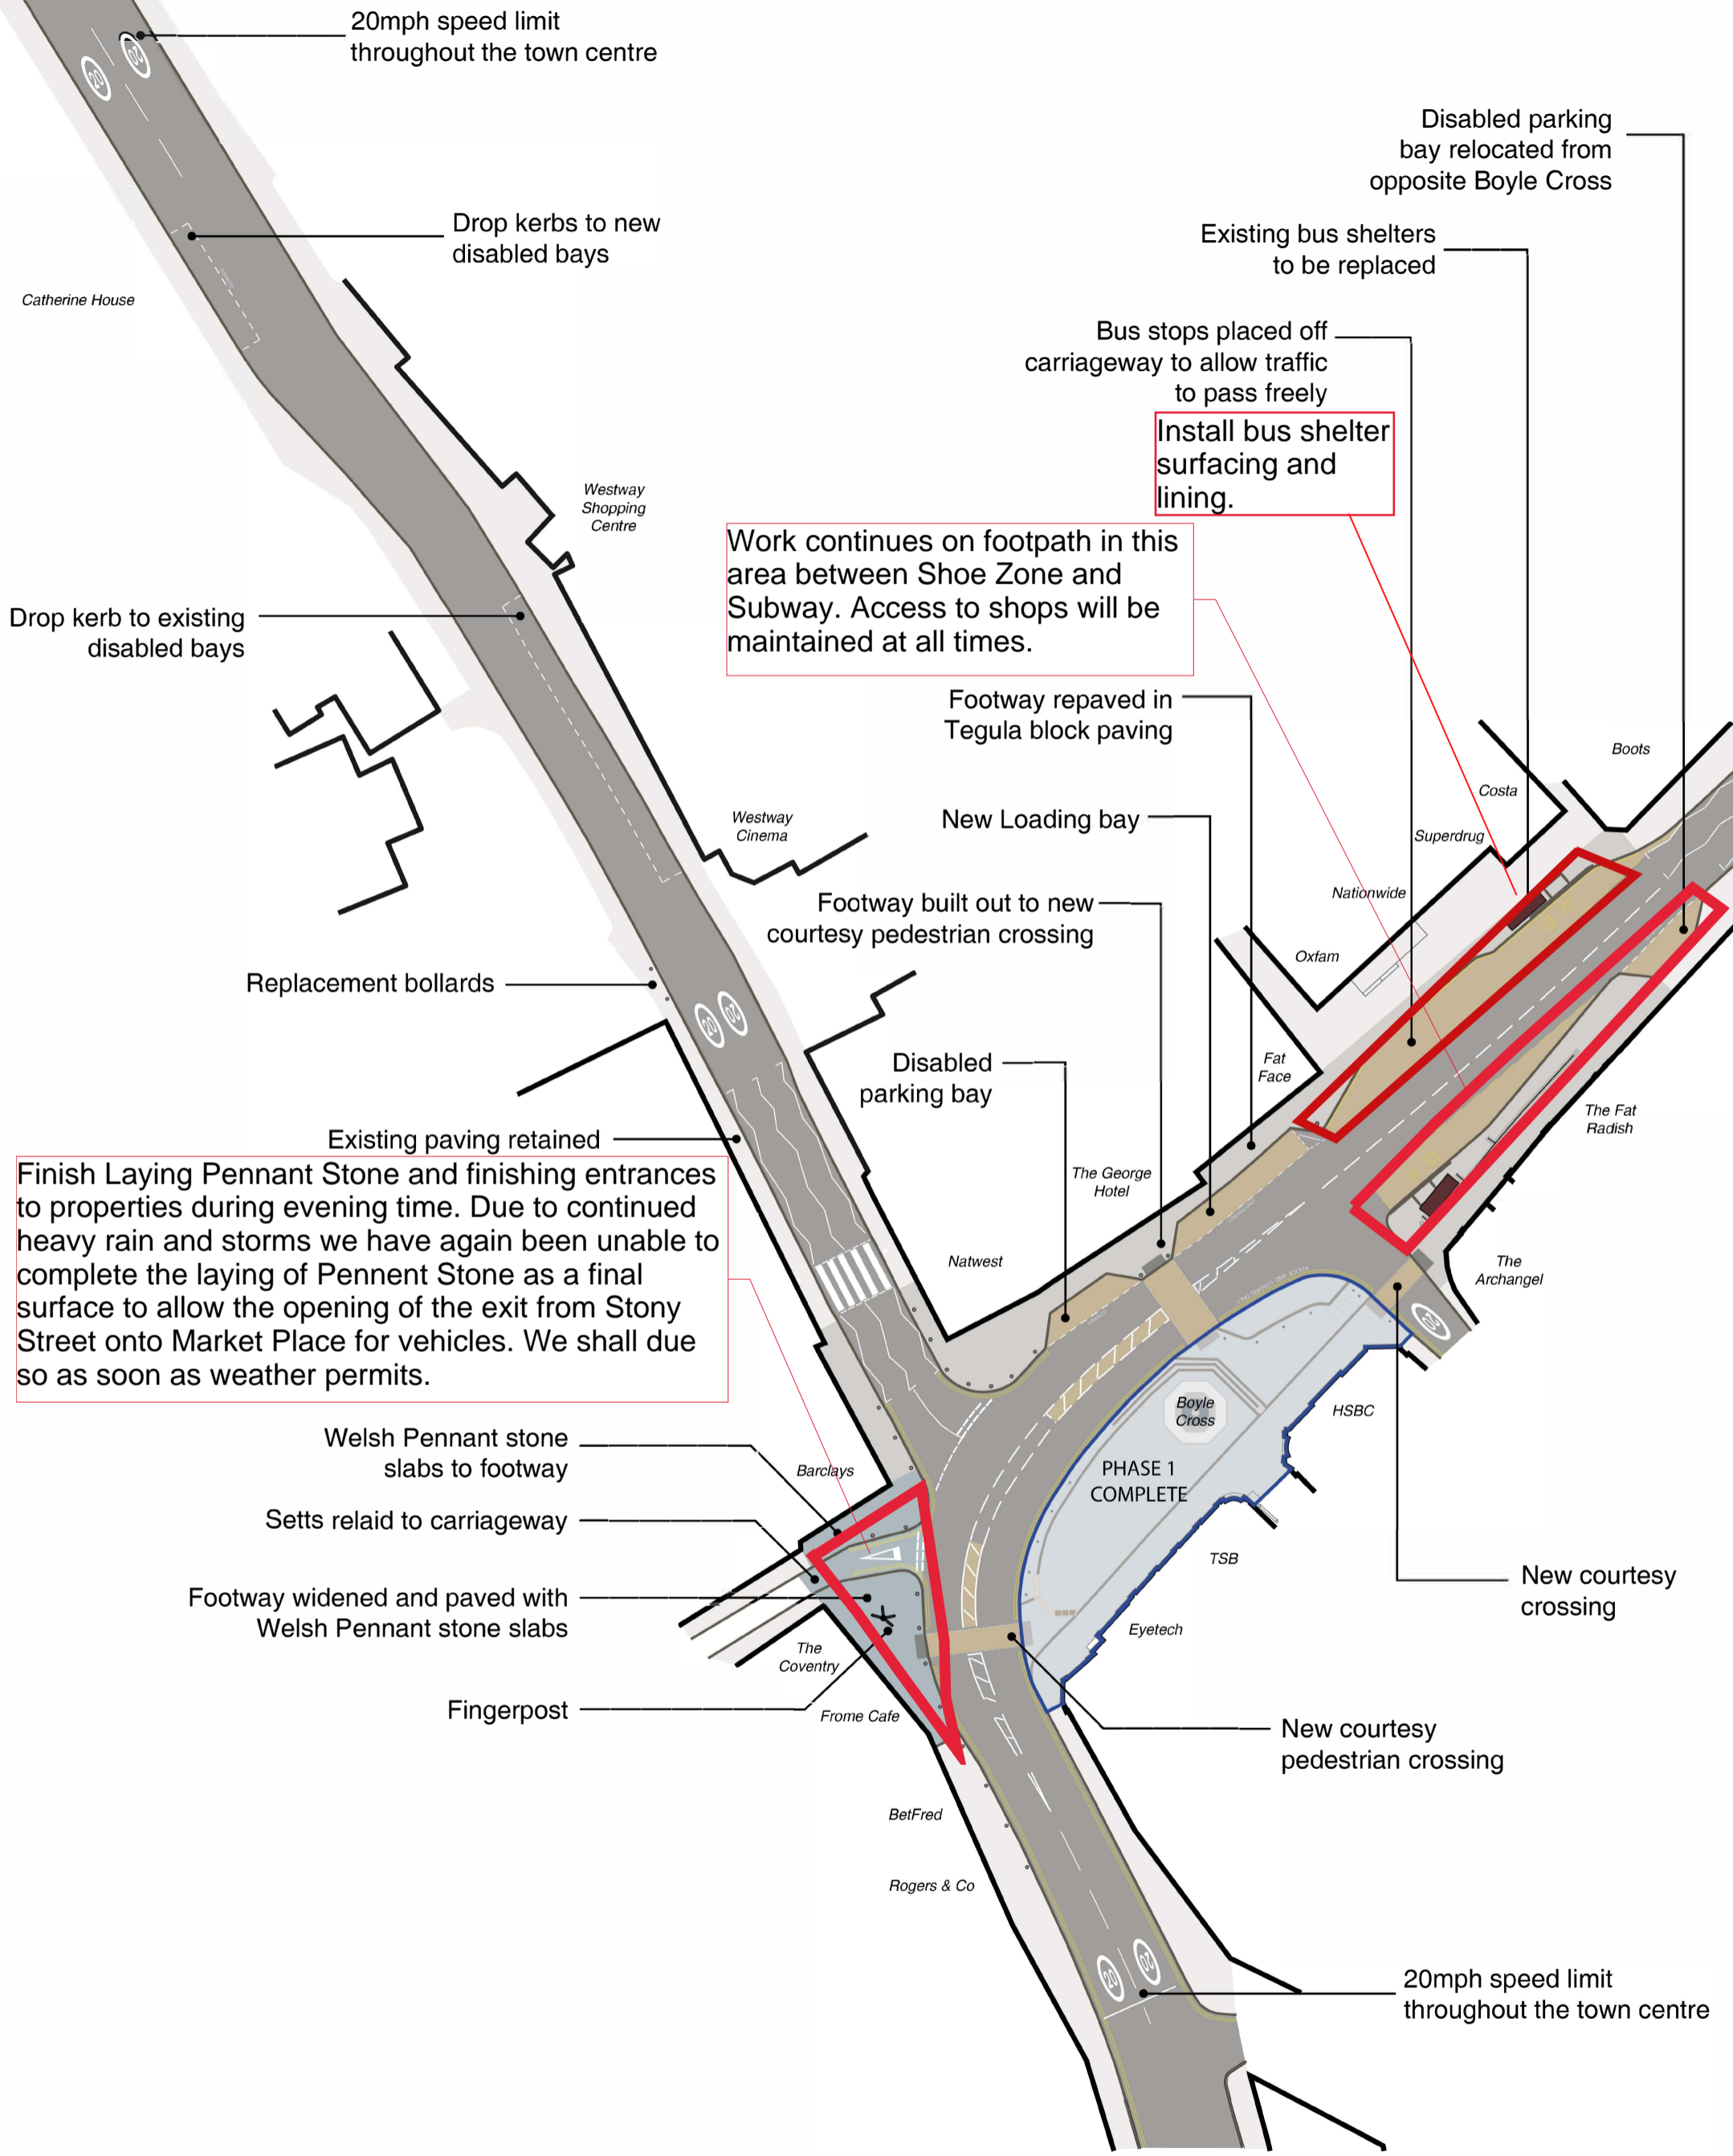

Finish Laying Pennant Stone and finishing entrances to properties during evening time. Due to continued heavy rain and storms we have again been unable to complete the laying of Pennant Stone as a final surface to allow the opening of the exit from Stony Street onto Market Place for vehicles. We shall do so as soon as weather permits.

Work continues on footpath in this area between Shoe Zone and Subway. Access to shops will be maintained at all times.

Install bus shelter surfacing and lining.

PHASE 1 COMPLETE
